

Northern Line Extension

Kennington Park

Community Liaison Group

30 01 2017

Delivering the Northern line extension with

ferrovial
agroman




MAYOR OF LONDON



Kennington Park Oct 2016 – Jan 2017

- Completion of 9.5m step excavation
- Commencement of 6.5m step excavation and ring erection

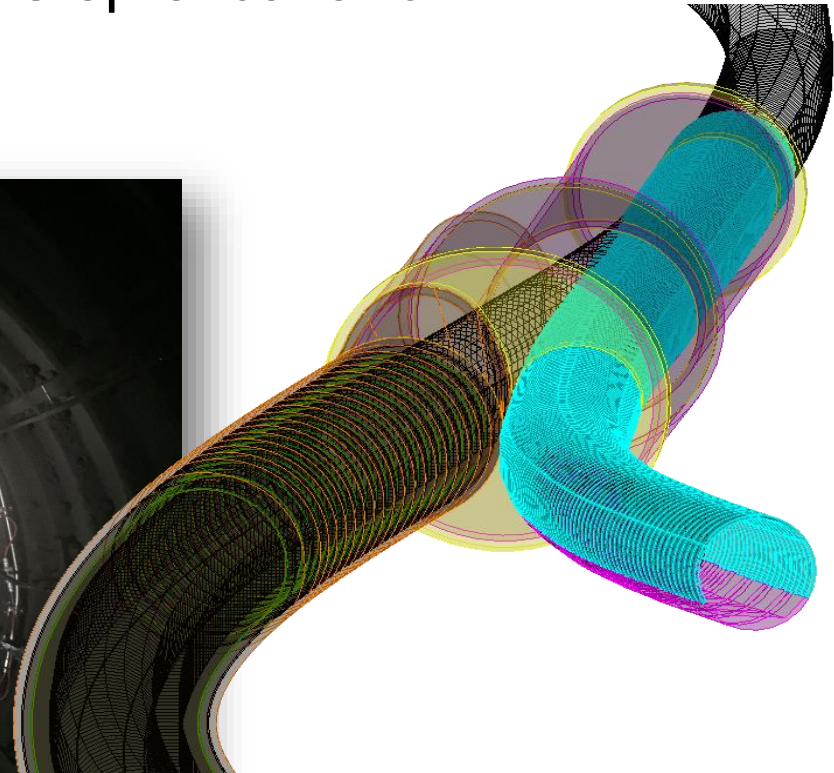

Kennington Park – Oct'16 - Jan 2017



FERROVIAL AGROMAN
LAING O'ROURKE JV



*SCL Pilot tunnel excavation. W/C – 03/10/2016



SCL over dig W/C – 10/10/2016



*Spray concrete lining



Kennington Park – Oct'16 - Jan 2017



Installation of propping following excavation WC – 17/10/2016

Kennington Park – Oct'16 - Jan 2017



FERROVIAL AGROMAN
LAING O'ROURKE JV



Completion of SCL and main propping WC – 31/10/2016



Kennington Park – Oct'16 - Jan 2017



Timber heading excavation WC – 07/11/2016

Kennington Park – Oct'16 - Jan 2017



FERROVIAL AGROMAN
LAING O'ROURKE JV




Timber heading excavation WC – 07/11/2016
New foundations for track commence pouring



Kennington Park – Oct'16 - Jan 2017



FERROVIAL AGROMAN
LAING O'ROURKE JV

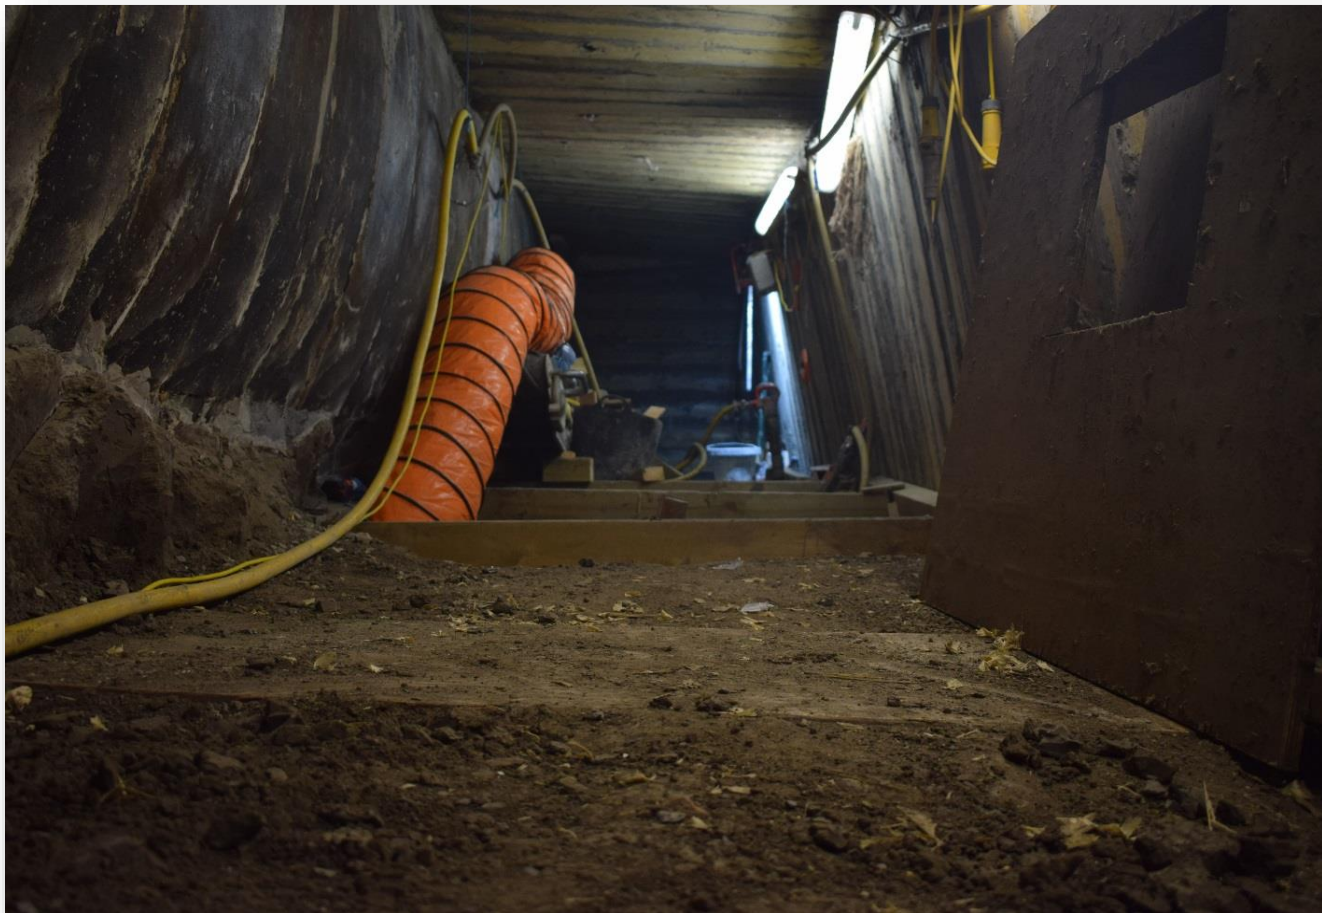


Tight sight of timber heading excavation with live loop on left W/C – 14/11/2016



Kennington Park – Oct'16 - Jan 2017



FERROVIAL AGROMAN
LAING O'ROURKE JV

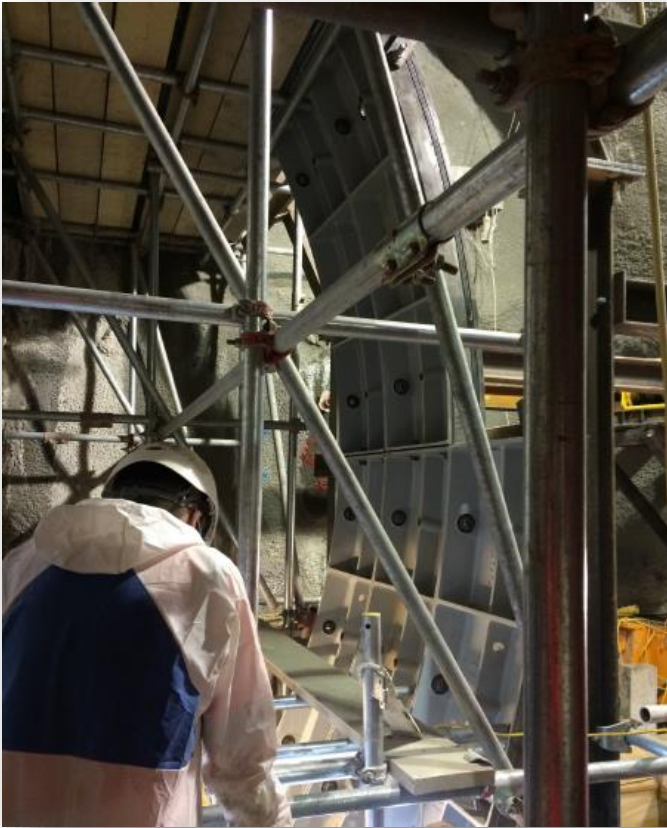

Installation of SGI rings
W/C – 09/01/2017




First permanent SGI rings installed
W/C – 23/01/2017




Kennington Park Step Plate Junction (SPJ) Look Ahead

- Completion of 6,5m excavation and ring erection SPJ April '17
- Completion of 9,5m ring erection SPJ June '17
- Completion SPJ including headwall concrete pours July '17

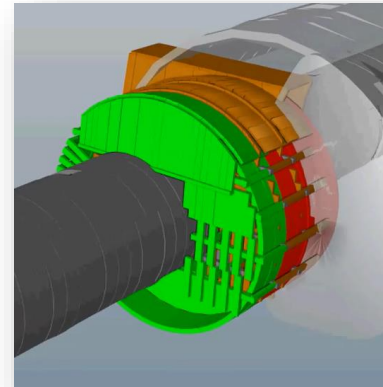

SGI ring installation


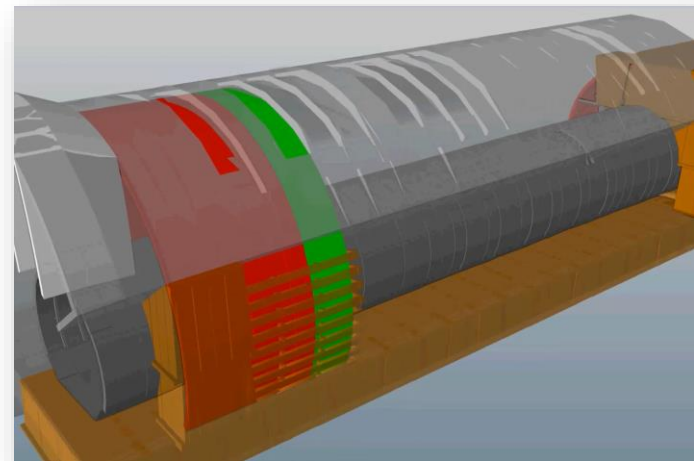


Headwall construction

Kennington 2017 possessions

- Possessions for delivery of NLE Track works to tie into Kennington Loop are planned for:
 - 16-17 Sep '17
 - 30 Sep- 1 Oct '17
 - 14-15 Oct '17
- 3 x 52h weekend possessions
 - 16-17 Sep '17
 - 30 Sep- 1 Oct '17
 - 14-15 Oct '17
- 10-day Christmas '17 blockade
 - 23 Dec '17 - 1 Jan '18

All closures subject to change if LU need to operate a service or if an emergency occurs

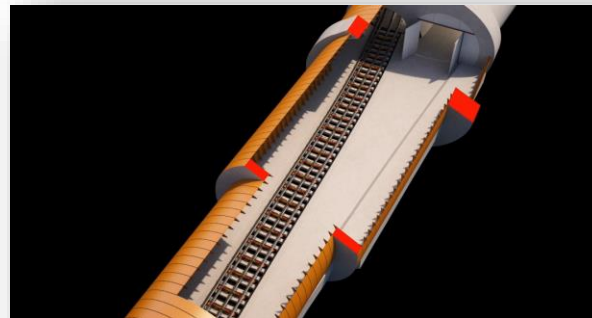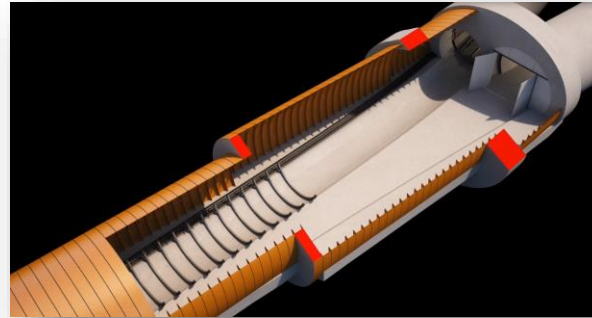

Kennington sites Logistics



FERROVIAL AGROMAN
LAING O'ROURKE JV

Lorry movements significantly reduced from Jan 17


Cleaning of the road McGovern road sweepers 4 times a week the Montford/Kennington sites, but we can call the sweepers out on request.

We continue to Work Related Road Risk driver training awareness for vulnerable road users, IE cyclists.


WRRR auditing deliveries, where all wagons on site were randomly inspected, concluding all wagons on site were 100% compliant.

Abnormal deliveries – We (FLO) advise all deliveries requesting to deliver abnormal loads to the NLE to alert the metropolitan police, as this will aid in reducing congestion and ensure the safety of the delivery to its destination.

Similarly, once the metropolitan police have authorised the delivery, we alert the residents under section 61 explaining the reasons for either working early/late. In addition, there are no planned abnormal loads at present.

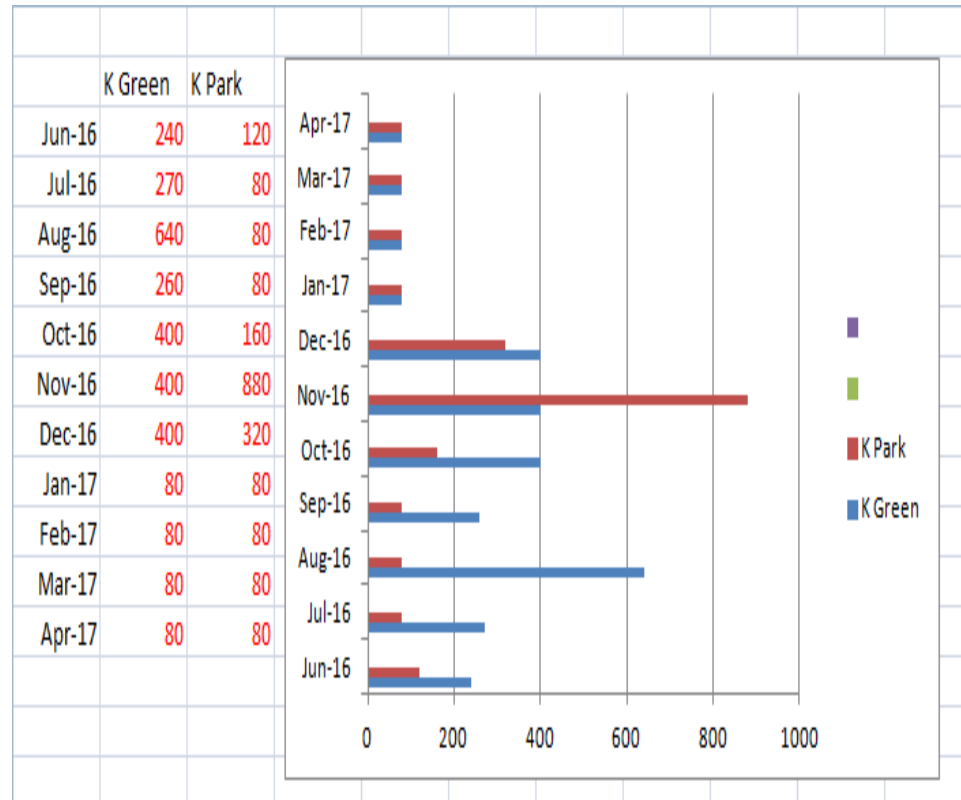

Environmental Monitoring Locations



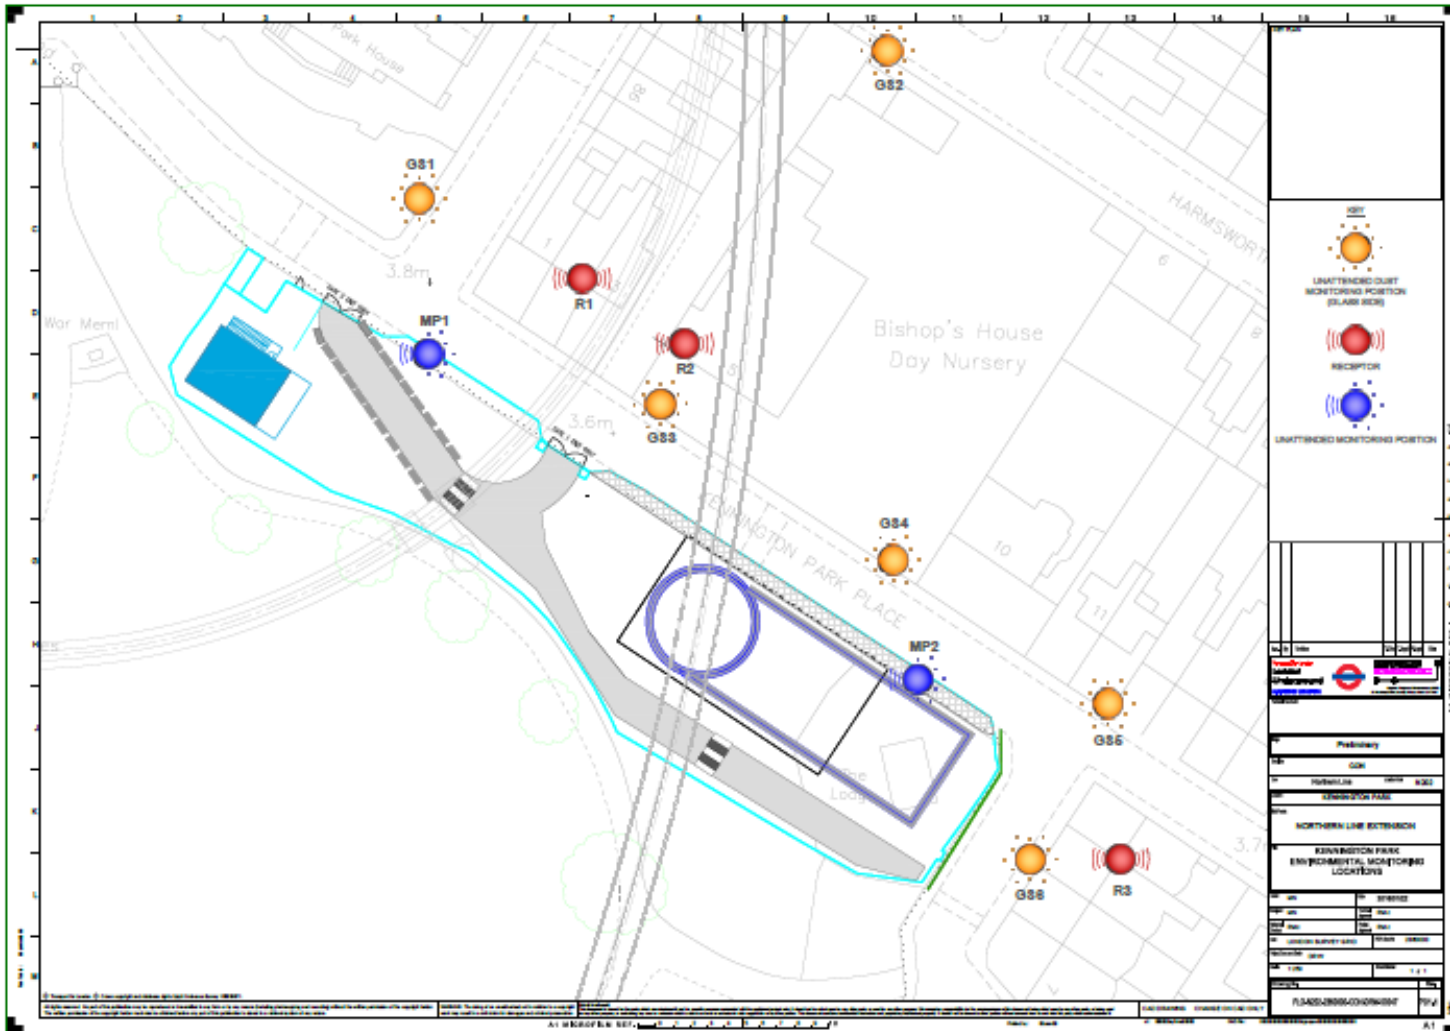


Monitoring OCT – DEC 2016

Environmental Monitoring



FERROVIAL AGROMAN
LAING O'ROURKE JV

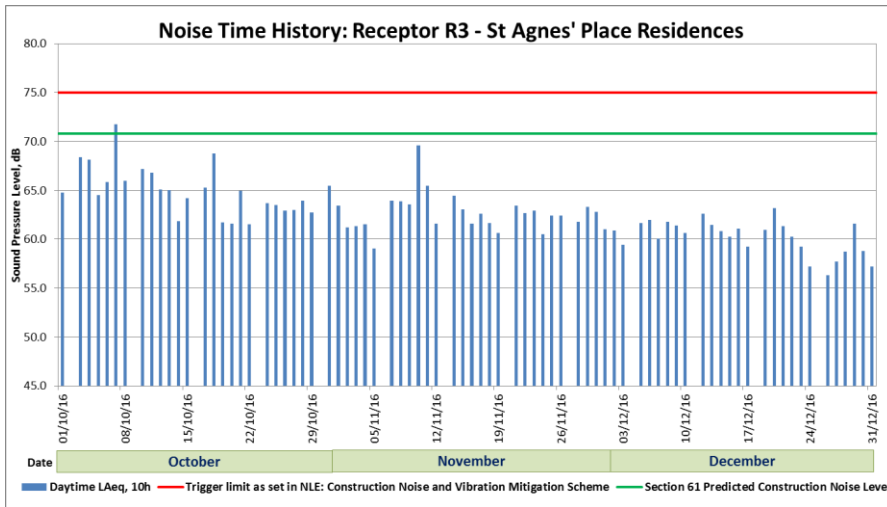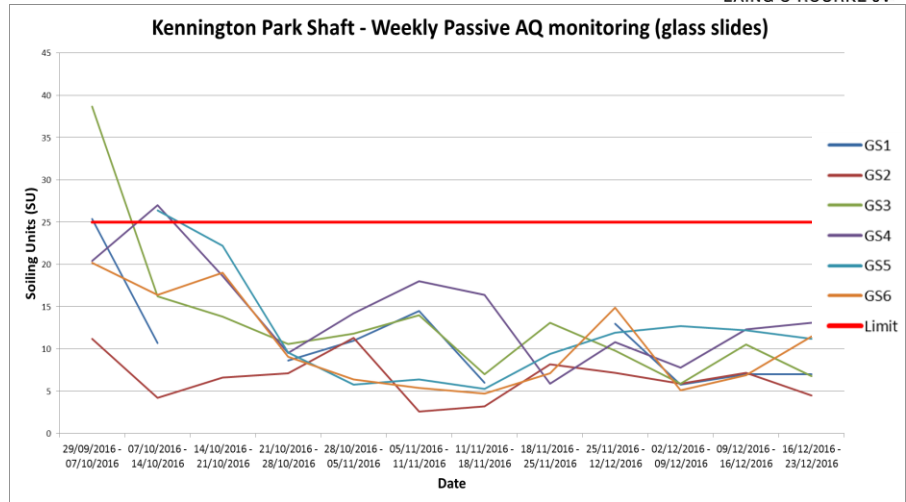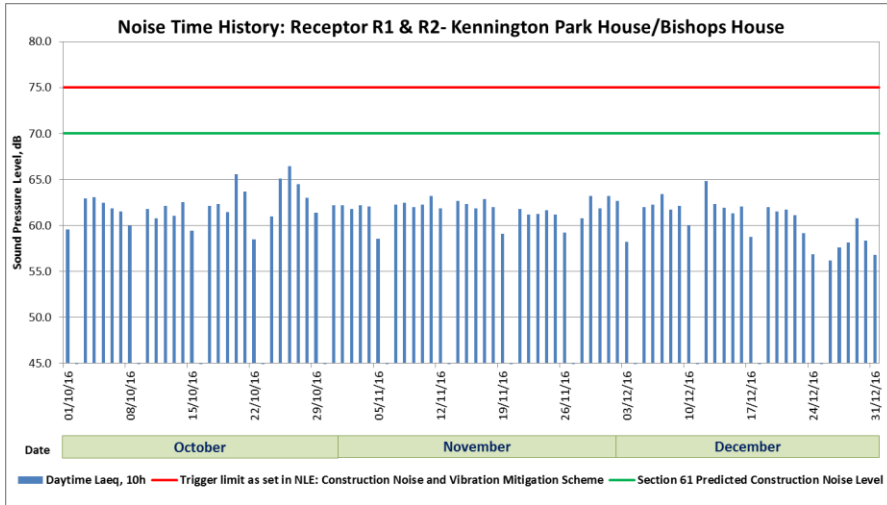

During these three months of monitoring there were zero noise triggers. Noise values have been within the Section 61 predictions.

Regarding night time triggers, there were no triggers for the months of October and December. However, there were 9 times in November where the level exceeded the agreed limits, all of are attributed to non NLE activity including: emergency sirens, traffic noise and fire work events.

Dust deposition rates have been lower than guidance criterion of 25 SU per week set out by the Environmental Agency, with the exception of the end of September / beginning of October.



Kennington Park Working Hours

- Excavation of the shaft and tunnels
continues to be 24/7
- Core hours are 08:00 to 18:00
Monday to Friday and Saturday
08:00 to 13:00 for surface works.
- NLE have applied to Lambeth to
allow for deliveries of cement over
the weekend, as a contingency
- NLE always look to apply 'Best
Practicable Means'



Your Feedback

Feedback	Action
Jet washers producing noise	New equipment was procured. Electrical, thus less intrusive. Resident thanked.
Cracks and sticking doors process	One to one visits to affected properties are organised regularly Reimbursement for repairs is on going
More engagement with schools and youth	We have re visited the Kennington Park Academy and started a pilot programme with Sacred Heart School
Proactive engagement ahead of works	Letter drop and door knocking to future impact properties
Step Plate Junction information	A session was held at Durning Library 10 Nov '16
More engagement about the Head house and Landscaping	A session was held at Kennington Park community centre 23 Nov 16
Engagement with Local MPs and members of GLA	We hosted a visit for GLA members on Oct 27



Complaints Summary




FERROVIAL AGROMAN
LAING O'ROURKE JV

Since Sep 16...


- 332 contact cases since
- 52 of these cases are still active
 - 20 are active complaints
 - 32 are active enquiries

All Cases

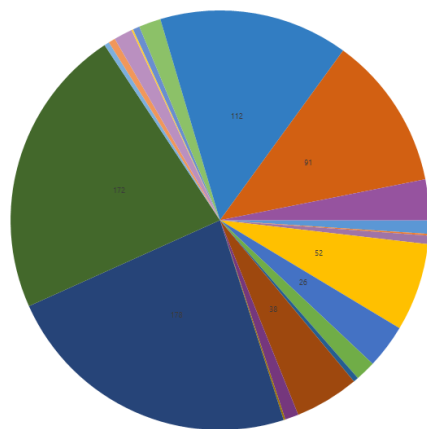


Open Cases / Closed Cases

Open Cases / Closed Cases

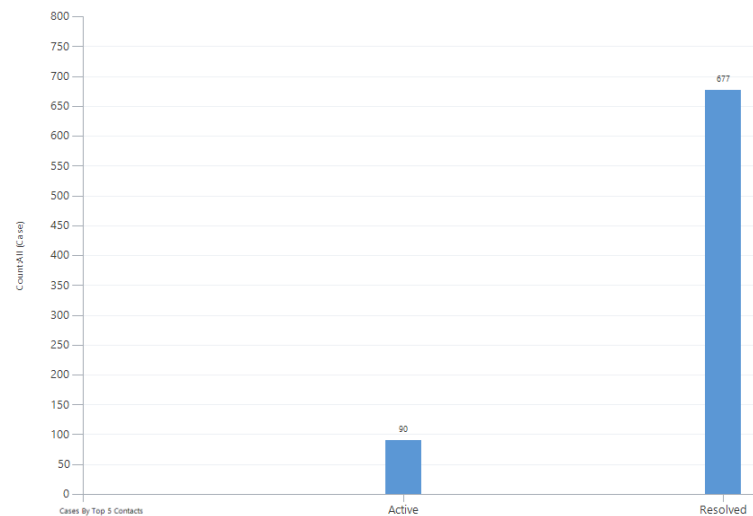

Cases By Top 5 Contacts

Cases By Top 5 Contacts

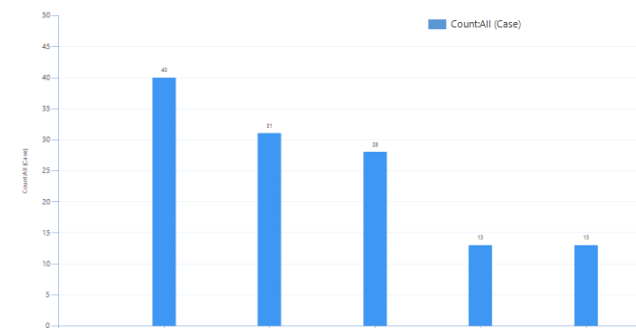

NLE Engagement Opportunities



FERROVIAL AGROMAN
LAING O'ROURKE JV

- CLG meetings
- One to one meetings
- Drop in sessions
- School and Youth



Engagement

- Stakeholder Activities
- LEAP group meetings
- Cycling safety Events



NLE Skills and Employment



FERROVIAL AGROMAN
LAING O'ROURKE JV

SLNT schedule

	Performance against Targets				SLNT Value equals	SLNT Value	
	Employer Overall	Yr 1 Target	Y1 Actual	Yr 2 Target			Y2 Actual
Apprenticeships	56	4	6	4	17		
Apprentice starts	22	4	6	4	15		
Apprentice completions	14	0	0	0	2		
Workless Job Starts	41	6	6	6	41	1	
Job Starts	41	6	6	6	41		
Graduates	21	4	13	4	4	1	
Graduate starts	21	4	13	4	4		
Taster Positions	200	35	109	45	64	100	
Work Experience Placements - Students In Education (school, colleg	70	15	55	15	39		
Work Experience Placements - Pre-employment and other Pathways	130	20	54	30	25		
Placement Positions	400	50	223	100	576	200	
Summer placements - FE Construction Diploma levels 1 and 2	200	25	0	50	0		
HE Work Placements - Under/ Graduates	200	25	223	50	576		
Adult Apprenticeship	30	3	3	8	2	1	
Existing Apprentices	30	3	3	8	2		
Workforce Skills	800	100	386.55	125	322.6	100	
NVQ starts for subcontractors	73	10	0	10			
Diversity training for existing workers	200	25	0	34			
H&S Tests leading to competence cards for Contractor's team	25	5	27	5	27		
Short courses for subcontractors team	400	50	239.55	60	235.6		
Accredited training	100	10	53	15	59		
Professional membership - CIOB / ICE / RICS	2	0	1	1	1		
Educational Activities	400	50	35.25	80	28.85	50	
Schools Activities (resource days)	150	30	1.75	30	8.85		
Curriculum Support Events	25	2	11.5	7	11		
Site Visits - Schools	75	10	0	15	0		
Site visits - Further Education	50	5	0	10	0		
Site visits - Higher Education	25	2	0	3	0		
HEI Industry interaction	25	5	0	5	0		
Ambassadors training	50	10	22	10	9		
Total		252	609.5	372	732.85	Total Target Points	Total Achieved
		19.6	32.0	25.8	71.323	164	0

- 27 Positions advertised through local brokerages – 8 completed.
- Work experience – ongoing with local schools across Southwark, Lambeth & Wandsworth
- BEST (Business Education Succeeding together)
- Working with TfL on their pre-employment pilot scheme aimed to get young people from the local area upskilled and into apprenticeships



Gabriel Jetawo's (pictured above) and Brian Linden, founder of Second Chance.



Construction Youth Trust pilot-scheme, Foundations for the Future. 5 workshops in 1 year. Sacred Heart School in Kennington



Ways to contact us

- It is important that calls are logged through the NLE 24/7 helpdesk on 0343 222 2424 (Option 1)
- Email nle@tfl.gov.uk
- Drop In sessions
- Please visit:

<https://tfl.gov.uk/northern-line-extension>
